ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		Mobilization & Saw Cutting	1 day	Mon 10/14/24	Tue 10/15/24		
2		Storm - Starting at Pennsylvania and working East.	6 days	Tue 10/15/24	Thu 10/24/24		
3		Curb & Guter Prep	2 days	Thu 10/17/24	Mon 10/21/2		
4		Withrow pour Curb & Gutter	1 day	Tue 10/22/24	Wed 10/23/24		
5		Sidewalk & pathway Prep Starting at Pennsylvania	2 days	Tue 10/22/24	Thu 10/24/24		
6		Withrow pour Sidewalk & ADA ramps	2 days	Mon 10/28/24	Wed 10/30/24		
7		HMA Paving	1 day	Thu 10/31/24	Fri 11/1/24		
8		Punchlist & Clean up	2 days	Wed 10/30/2	Fri 11/1/24		

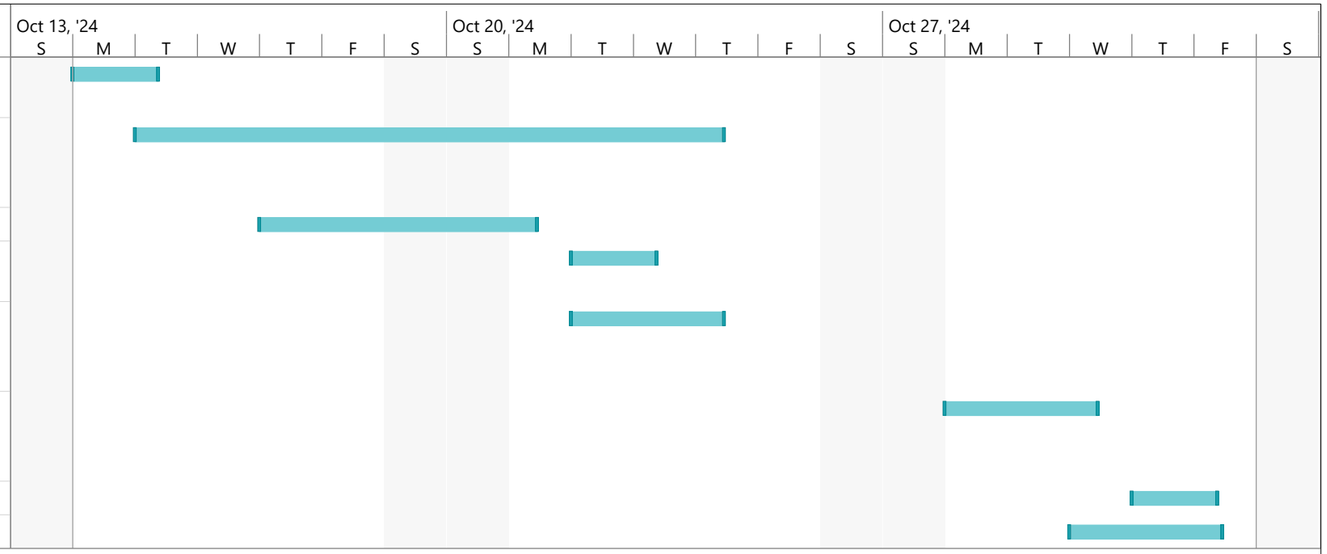

Project: Cle Elum 2nd Street Pa
Date: Thu 10/3/24

Task	Project Summary	Manual Task	Start-only	Deadline			
Split	Inactive Task	Duration-only	Finish-only	Progress			
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress			
Summary	Inactive Summary	Manual Summary	External Milestone				
